Capital Asset Advisory Committee 2018 Capital Improvement Program Financial Status June 30, 2020

July 2, 2020





Revenue

- \$ (326,490,000) First Bond Issuance
- \$ (50,165,349) Premium on First Bond Issuance
- \$ (11,646,527) Interest Through May 31
- \$ (20,900,481) Fiscal Year 2020 Capital Transfer (COP Principal & Interest Payment Removed)
- \$ (409,202,357)

Expenses

Δs	of	lune	30.	2020
$\boldsymbol{\neg}$	VI.	Julic	JU.	2020

- \$ 126,558,504 Total Expended All projects
- \$ 157,681,682 Total Encumbered All projects


As of May 31, 2020

- 109,417,007 Total Expended All projects
- \$ 147,814,548 Total Encumbered All projects

Charter Projects

- \$ 25,163,874 Total Expended Charter
- \$ 6,319,367 Total Encumbered Charter

- \$ 24,524,558 Total Expended Charter
- \$ 2,251,911 Total Encumbered Charter





Funding Breakdown 2018 Capital Improvement Program

\$ 326,490,000	First Bond Issuance
\$ 50,165,349	Premium on First Bond Issuance
\$ 11,646,527	Bond Interest Through May 31, 2020
\$ 20,900,481	FY 2020 Capital Transfer
\$ 409,202,357	Funds to Date
\$ 240,510,000	Estimated Second Bond Issuance
TBD*	Premium on Second Bond Issuance
TBD*	Future Bond Interest Earnings
\$ 104,502,405	5 Years Capital Transfer
TBD*	Interest on Capital Transfer
\$ 754,214,762	Preliminary Total

TBD* To Be Determined





Additions, New Buildings & In Design to Bid Late Summer / Fall

Additions

Bell MS Addition - Bid Date July 2020 Foster ES Addition - Bid Date October 2020 Wayne Carle MS Addition - Bid Date September 2020 Manning K8 Addition - Bid Date July 2020 Parmalee ES Addition - Bid Date September 2020

New Building

CTE South - Bid Date August 2020

In Design

Pomona High School Addition/Renovation

Jefferson High School Addition/Renovation — GMP July 2020

Lumberg Elementary School Addition/Renovation

Fall Design Starts

Marshdale Elementary School Replacement Prospect Valley Elementary School Replacement Ralston Valley HS Addition/Renovation Standley Lake HS Addition/Renovation



Under Construction:

Arvada HS Addition / Renovation

Three Creeks K8 Addition

Wilmot ES Addition / Renovation

Kendrick Lakes ES Replacement

Columbine HS Addition / Renovation

Green Mountain HS Addition / Renovation

Conifer HS Addition / Renovation

6 HS Artificial Turf & Tracks

Alameda International Jr./Sr. High School

Complete August 2020

Complete

Complete August 2020

Complete December 2020

Complete July 2021

Complete July 2021

Complete July 2021

Complete August 2020

Complete August 2022

Furniture:


14 replacements

Columbine HS Partial Replacement

Green Mountain HS Partial Replacement





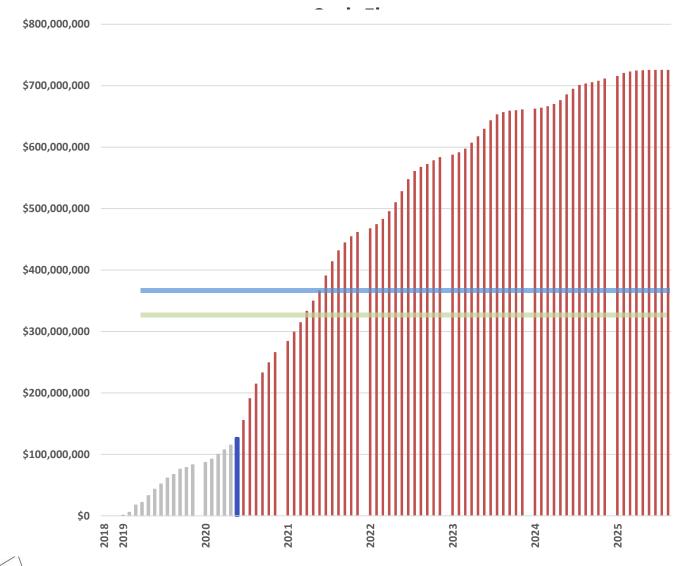



CAPITAL IMPROVEMENT PLAN – FINANCIAL STATUS 5/31/2020

Impact of COVID-19 Virus

To date there has been minimal impact from Covid-19 on the availability of labor or materials to on-going projects.

Projects in design or under construction are continuing normally.








CAAC Construction Update

7-2-2020



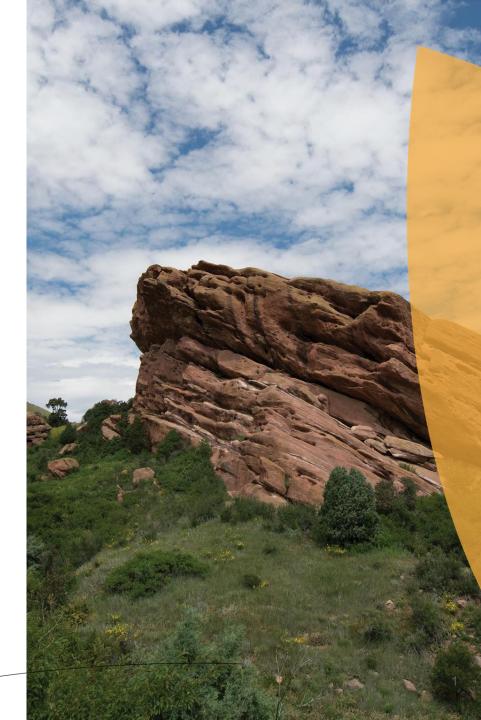

2020 - PROJECTS

58 of 88 Elementary Schools

11 of 15 High Schools

6 of 17 Middle Schools

2 of 2 7-12 Schools

2 of 6 K-8 Schools

7 of 18 Option Schools

1 of 4 Athletic Facilities





Alameda HS – Addition WOLD – CMGC Phipps





Conifer HS – Addition Cannon – CMGC FCI







Green Mountain HS – Addition MOA – CMGC GE Johnson

Construction





2020 HS Field Improvements Green Mountain HS HCM – CMGC ECI



Columbine HS – Addition EIDOS – CMGC Swinerton

Construction

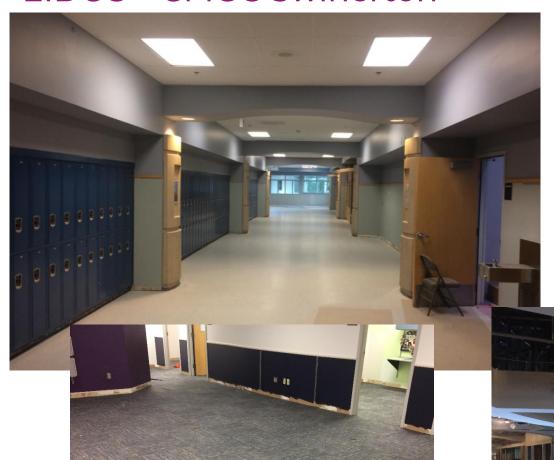



2020 HS Field Improvements Columbine HS HCM – CMGC ECI





2020 HS Field Improvements A WEST HCM – CMGC ECI





2020 HS Field Improvements Golden HS HCM – CMGC ECI







2020 HS Field Improvements Pomona HS HCM – CMGC ECI





2020 HS Field Improvements Standley LakeHS HCM – CMGC ECI








Arvada HS - Addition HCM – CMGC Saunders



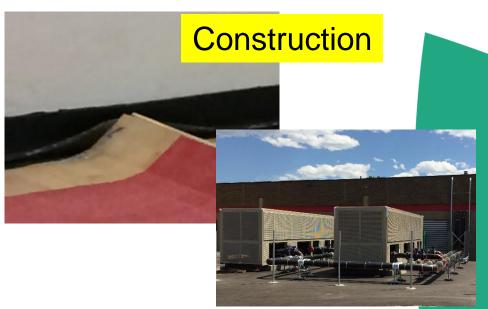



Complete


District Wide LED Site Lighting Ackerman – Piper Electric





Security Glass Installation 14 - Elementary Schools

Kyffin ES	Mitchell ES	
Complete	Complete	
Stevens ES	Thomson ES	
Complete	85%	
Peck ES	Warder ES	
Complete	Complete	
Secrest ES	Wilmore Davis	
Complete	Complete	
Grn Mtn ES	Elk Creek ES	
Complete	50%	
Sheltion ES Complete	Edgewater ES	
Slater ES Complete	Shaffer ES	

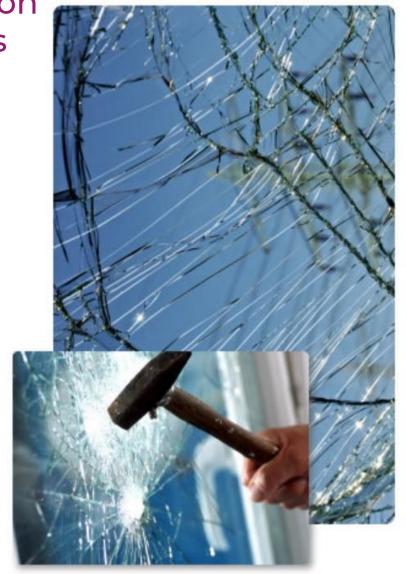



Security Camera Installations Elementary Schools – Final Installations Middle Schools – Starting





West Jefferson MS – Upgrades Cannon – CMGC FCI





Three Creeks K8 – Addition HCM – CMGC Phipps

Complete Punch List





Wilmot ES – Addition DLR – CMGC Himmelman


Construction
August 2020
Completion





DW LED - 18 Schools Ackerman – CMGC Weifield



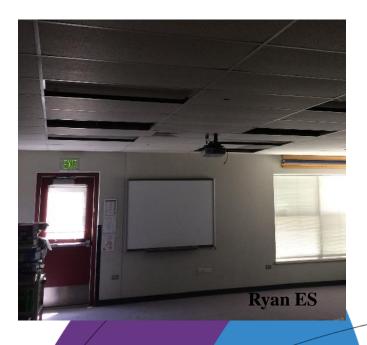


- 1. Columbine Hills ES
- 2. Deane ES
- 3. Devinny ES
- 4. Dennison ES
- 5. Fitzmorris ES
- 6. Kullerstrand ES
- 7. Lasley ES
- 8. Maple Grove ES
- 9. Patterson International
- 10. Peck ES
- 11. Powderhorn ES
- 12. Ryan ES
- 13. Secrest ES
- 14. Sheridan Green ES
- 15. Stott ES
- 16. Vanderhoof ES
- 17. Westgate ES
- 18. Westridge ES



Kendrick Lakes ES – Replacement Larson Incitti – GC Roche

Construction

Dec. 2020 Completion

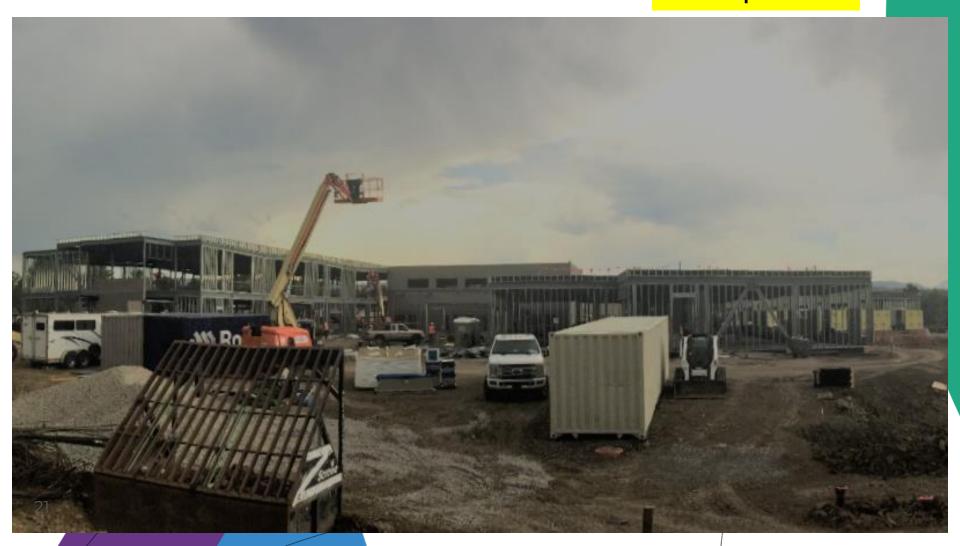

DW Roofing I – Green Mtn, Lasley WJE – CMC & United Materials



Construction

Green Mtn ES 35%


Lasley ES 25%





Complete

Chiller Replacement – Golden HS Columbine – K&M

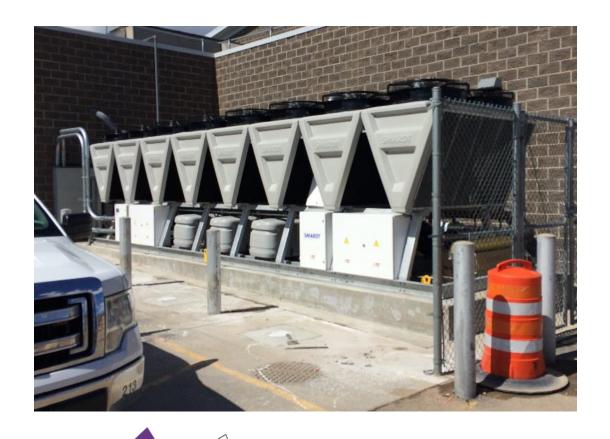




DW Roofing I - Patterson ES, Par ES, Thomas ES WJE –United Materials, Flynn



Construction

Parr 90%

DW Mechanical – Patterson ES Columbine - Braconier

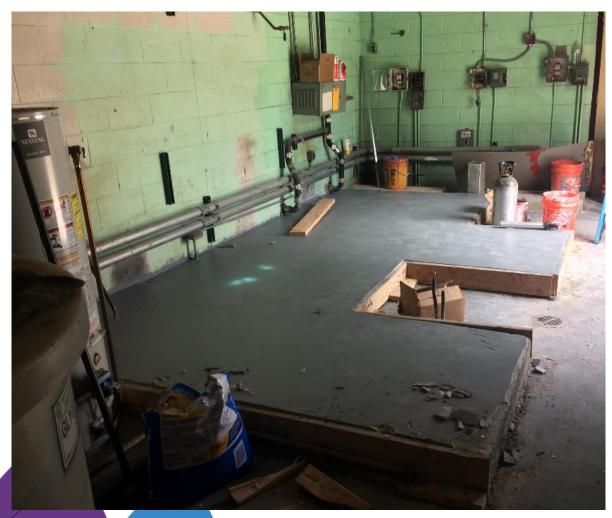



DW Mechanical – Stott ES RTU,

Construction
Set RTU
7-1 to 7-6

Columbine - Braconier






DW Mechanical - Ryan ES RTU


Construction
Set RTU
7-1 to 7-6

Columbine - Braconier

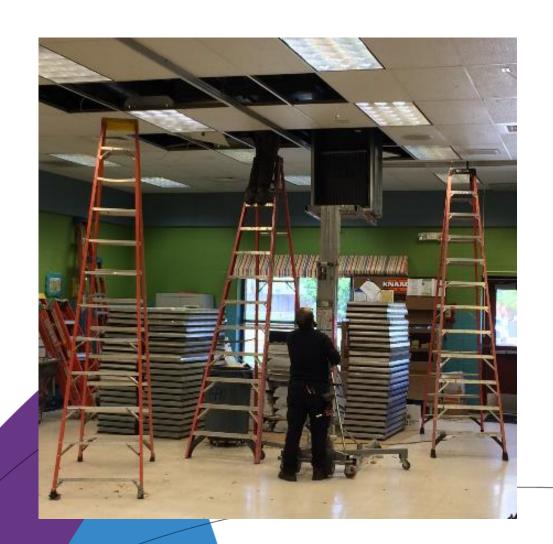



DW Roofing II – Evergreen HS Rooftech –Powers

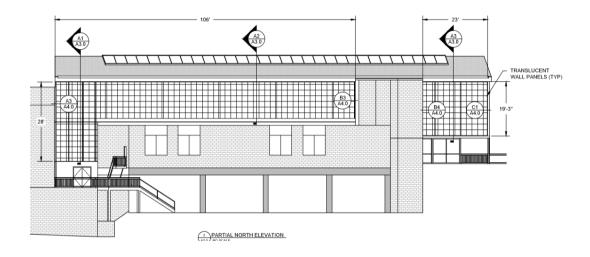

Construction \$148,700 EHS

Start 7/6



DW Roofing II – Kullerstrand ES

Rooftech - Grabau

Construction


70% complete







DW Roofing II – Carmody MS Rooftech - B&M

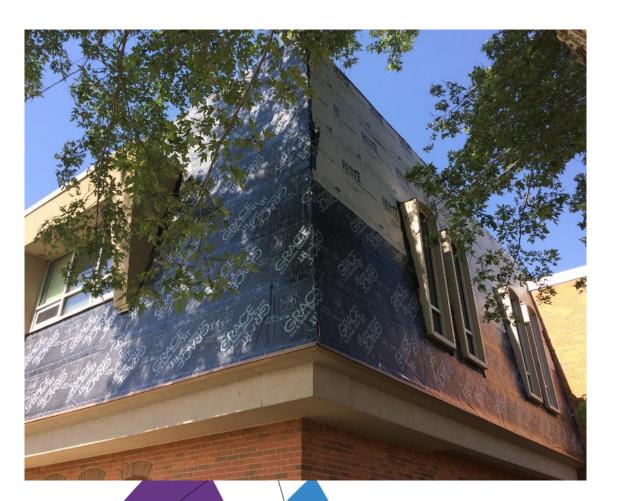

Construction

40% Complete





Trailblazer Locker Room & Press Box Mellin & Assoc. – WE O'Neal




AHU Replacement - Westridge ES Branch Pattern - JCOR



Set RTUs 7-7 to 7-10



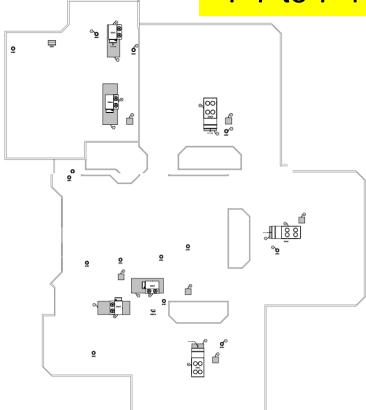



DW Playgrounds Allendale ES, Stott ES, Vanderhoof ES

Design Concepts - Richdale,





DW Playgrounds KendallvueES, Stony Creek ES, Westridge ES

Design Concepts –T2







DW Playgrounds Sheridan Green, Fletcher Miller

Design Concepts - Goodland






Eiber ES AMD - Himmelman



Belmar ES AMD – Palace Construction

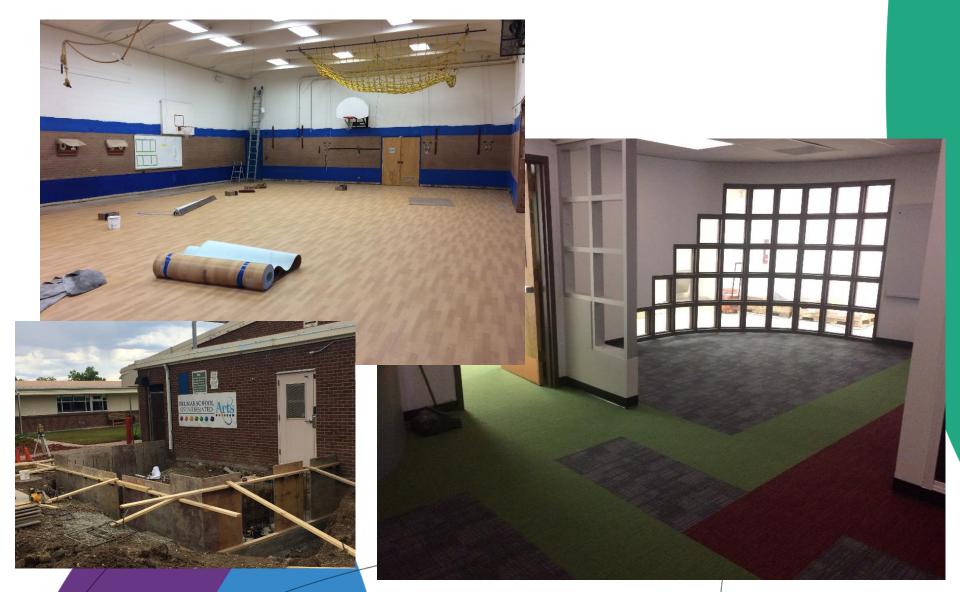

Columbine Hills ES Lawrence ES

Complete

Dadey -

Straightline










Green Gables ES Upgrades Sybazz – Himmelman

Construction



Hutchinson ES Upgrades Sybazz – Himmelman

Construction

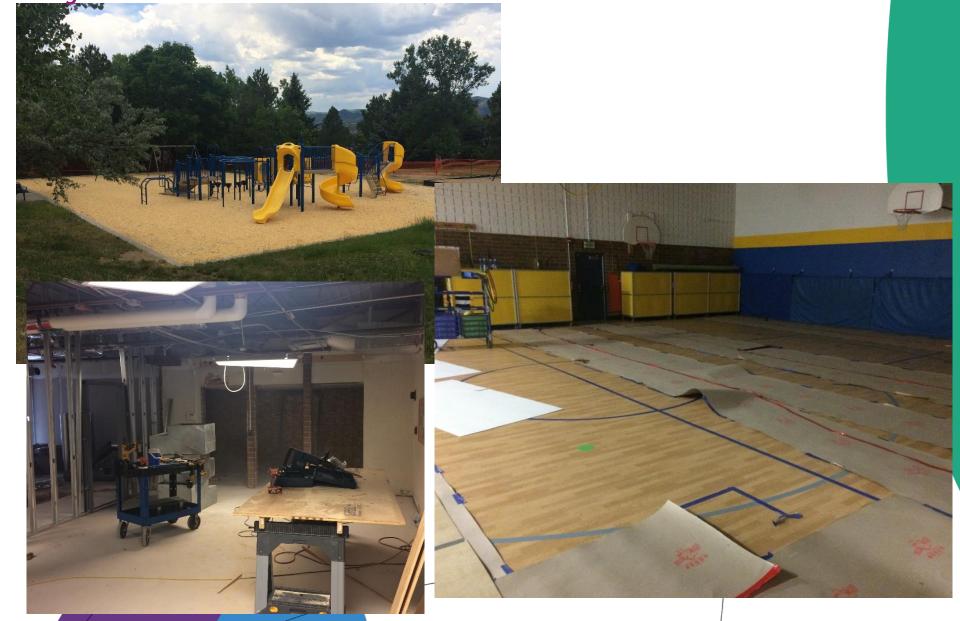

Ken Caryl – Signage & FACS Room Upgrades

Construction

HCM – Single Track



Dutch Creek ES – Upgrades

Construction

Cunningham Group - HPM







Adams ES – Upgrades RB+B – Palace Construction

Construction



Lukas ES – Upgrades

Construction

RB+B - Palace Construction



Semper ES - Upgrades

RB+B - Palace Construction







RB+B - Palace Construction



DW Paving II – Bradford Int, Ryan ES,


Mitchell ES, Shelton ES

JVA - Martin Marietta Materials







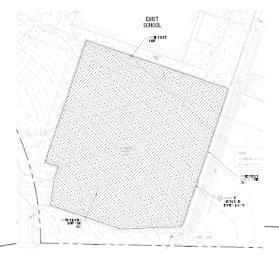



Construction

Ralston ES, Upgrades CRP – HPM






Foothills ES ES Upgrades CRP – Bryan

Construction







Vivian ES Upgrades CRP – Bryan

Construction RTU - OCT



Welchester ES Upgrades CRP – Bryan

Construction RTU - OCT






DW Flooring I - Fletcher Miller, Lasley ES, Free Horizon & Fitzmorris ES Farnsworth Group – HPM Contracting



RTA – GH Phipps

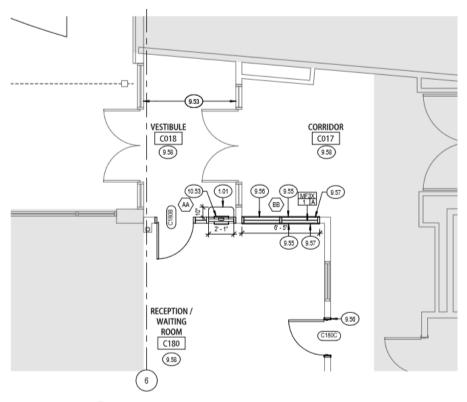








Arvada K8, Upgrades RTA – GH Phipps


Construction Chiller 7/24

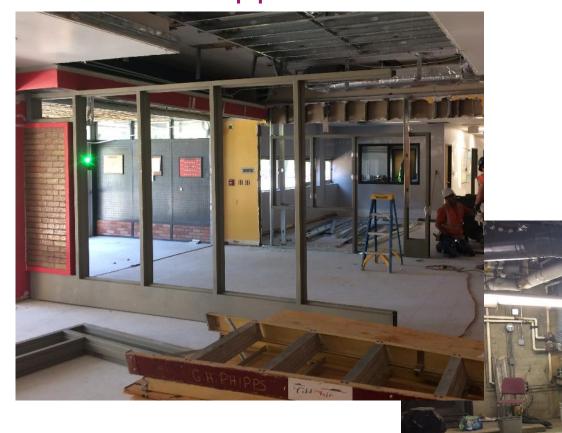




Fremont ES – Upgrades

Jordin - P.G. Arnold

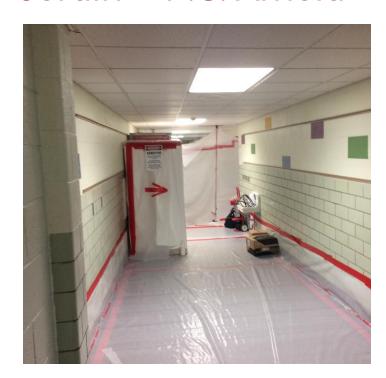

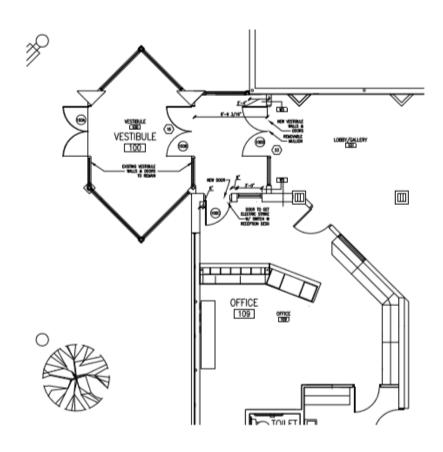






Coronado ES Upgrades

OZ - W.E. O'Neil

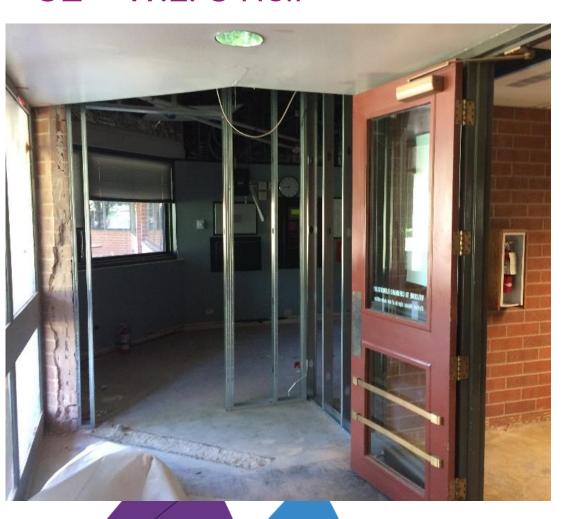

Construction Bid 3/27/20


\$1,657,000 \$35.60/sf



Columbine Hills ES Upgrades

Construction

OZ - W.E. O'Neil

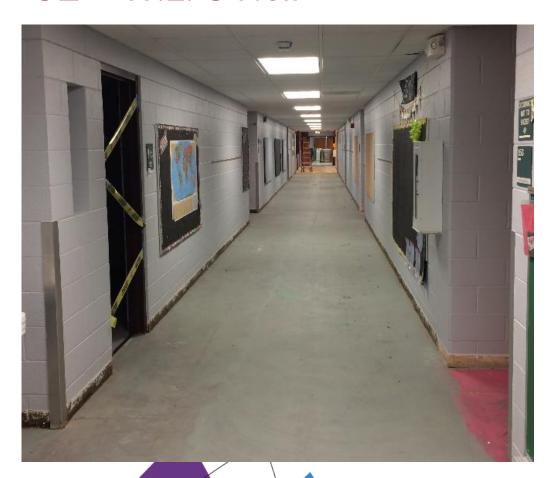





Stober ES Upgrades

Construction Alum SF - Aug

LOA – Golden Triangle



DW Flooring II - Allendale ES, Thomson ES, West Woods ES gym Fairmount gym & corridor EUA – Colorado Floorworks (FES) – Gary Leimer



In Design

New Construction & Additions

• START Construction SUMMER / FALL 2020



Bell MS – 1 Story,4 Classroom Addition Eidos – Contractor TBD

Construction Documents Bid 7/30





Manning Opt – 1 Story – 7 Classroom Addition AMD – Contractor TBD

Construction
Documents
Bid 8/13





CTE South – New Building HCM – Contractor TBD


Construction
Documents
Bid 8/20





Jefferson HS – Aux Gym Addition MOA – Haselden


Construction Documents





Lumberg ES – 4 CR Addition MOA – CMGC Haselden

Construction Documents





Parmalee ES – 1 Story – 5/6 Classroom Addition OZ – Contractor TBD

Construction Documents Bid 9/3





Wayne Carle – 2 Story – 8 Classroom Addition RB+B – Contractor TBD

Construction Documents Bid 9/17





Foster ES – 1 Story – 7 Classroom Addition Larson Incitti – Contractor TBD

Design
Development
Bid 10/15





Furniture

- Arvada HS
- Arvada K8
- Arvada West
- Bear Creek K8
- Belmar
- Columbine Hills
- Columbine HS
- Conifer HS
- Coronado ES
- Creighton MS
- Drake MS
- Dutch Creek
- Eiber ES
- Fairmount ES

- Foothills ES
- Free Horizon
- GMHS
- Green Gables ES
- Hutchinson ES
- Ken Caryl MS
- Kendallvue
- Kullerstrand ES
- Kyffin ES
- Leawood ES
- Lukas ES
- Maple Grove
- McLain HS
- Molholm ES
- Moore MS

- Normandy ES
- North Arvada MS
- Ralston ES
- Ralston Valley HS
- Rooney Ranch ES
- Ryan ES
- Stober ES
- Summit Ridge MS
- Three Creeks K8
- Ute Meadows ES
- West Jeff MS
- Welchester ES
- Westgate ES
- Wilmot ES
- Witt ES



2021 Projects (On Deck)

- DW Elevator
- DW Flooring
- DW LED
- DW Mechanical
- DW Paving
- DW Playgrounds
- DW Roofing
- DW Athletic Turf
- Allendale ES
- Carmody MS
- Chatfield HS
- Dakota Ridge HS
- Deane ES


- Dennison ES
- Devinny ES
- Evergreen MS
- Evergreen HS
- Everitt MS
- Fitzmorris ES
- Kullerstrand ES
- Lasley ES
- Lawrence ES
- Maple Grove ES
- Marshdale ES
- Miller Special OPT
- Patterson ES

- Pomona HS
- Powderhorn ES
- Prospect Valley ES
- Ralston Valley HS
- Ryan ES
- Sheridan Green ES
- Standley Lake HS
- Stott ES
- Vanderhoof ES
- Westridge ES



Pomona HS – Aux Gym Addition Sybazz – Saunders

Design Advisory Group

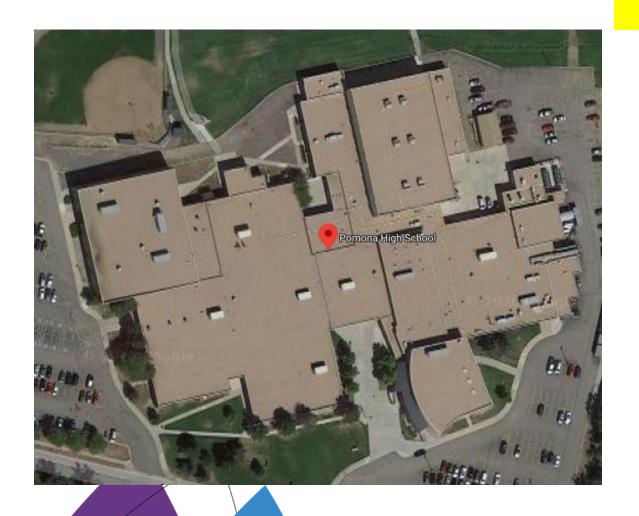



Next Meeting 8/6/20





2018 BOND PROGRAM COMMUNICATIONS UPDATE CAPITAL ASSET ADVISORY COMMITTEE JULY 2020

COMPLETED WORK:

- Published Bond Annual Report:
 - Shared on social media channels
 - Published on Jeffco Builds website
 - Will be shared in upcoming community newsletters from Jeffco
- Continued production of bond signs
- Worked with Lakewood Sentinel reporter on <u>Green Mountain construction project story</u>
- Sharing summer construction updates on Jeffco social media channels to keep the community informed of summer progress

Website analytics:

Jeffcobuilds.org and all pages with "jeffco builds" in the URL (ie sub-pages)

Jeffco Builds page performance	Page views	Unique page views
May 2020	1,893	1,159
June 2020	1,860	766
% change	1.4% decrease	33% decrease

UPCOMING WORK:

- Planning Warren Tech South news story and pitch:
 - Announcing program names
 - Sharing updated renderings
 - o Interviews with teachers and principal who will be at Warren Tech South
- Planning site tours of current construction projects for Facebook live videos





Nothing like a good time-lapse video to keep an eye on construction progress! As our contractors begin prepping for their work at Alameda International, they set up a camera so we can follow along. The school is undergoing a major makeover - with a major building addition with classrooms, a library, music/choral suite, new building entry, interior renovations, security enhancements, and updated furnishing. We will be sure to share more videos once the construction is in full swing!

If you want to know more about construction and projects happening across Jeffco, head over to Jeffcobuilds.org. #jeffcobuilds

